



Department for
Infrastructure

An Roinn

Bonneagair

www.infrastructure-ni.gov.uk

DfI ROADS WESTERN DIVISION

Report to

Mid Ulster District Council

Works Programme Update Autumn 2017

Photo: B73 Drumconvis Road, Coagh

CONTENTS**PAGE****Strategic Road Improvements**

- A6 Randalstown to Castledawson	4
- A29 Cookstown Bypass	5
- A5 Western Transport Corridor	6

Network Maintenance

Structural Maintenance

- Resurfacing Mid-Ulster (N)	8
- Resurfacing Mid-Ulster (S)	8
- Surface dressing - Mid-Ulster (N)	9
- Surface dressing - Mid-Ulster (S)	11
- Drainage – Mid-Ulster (N)	14
- Drainage – Mid-Ulster (S)	15
- Proposed footpath work – Mid-Ulster (N)	15
- Proposed footpath work – Mid-Ulster (S)	15

Network Development

Local Transport and Safety Measures

- Carriageways	16
- Pedestrian Measures	16
- Cycling Measures	17
- Traffic Calming	17
- Safer Routes to School	18
- Road Signs, markings & bollards	18
- Speed Limits	19
- Accessible Parking	19
- Local Transport & Safety Measures	20

Structures

- Bridge Management	22
---------------------	----

Street Lighting

- Planned works	24
-----------------	----

STRATEGIC ROAD IMPROVEMENTS

A6 Randalstown to Castledawson

The Regional Strategic Transport Network Transport Plan 2015 endorsed the provision of a continuous dual carriageway from the western end of the M22 at Randalstown to the Castledawson Roundabout.

Judicial Review

Part of the scheme has been subject to a Judicial Review, and the High Court found in favour of the Department. When the decision was appealed, the Court of Appeal upheld the original judgement.



Earthworks on the Randalstown to Toome section of the scheme

Both judgements confirmed the Department's robust economic, engineering and environmental assessment procedures enabling the Department to proceed with construction works across the entire scheme.

Construction Progress

Following extensive preliminary works advanced during winter 2016 and spring 2017, construction works on the Randalstown to Toome section and Moyola Bridge to Castledawson Roundabout section commenced in June 2017. Work on the remainder is also now ongoing, subject to environmental restrictions.

To date some 817,000m³ of earth, sourced from within the site, has been excavated and reused in embankment construction.

Construction of the Bellshill Overbridge, Moyola River Bridge, Drumderg Pedestrian Overbridge, Derrgowan Overbridge and Randalstown West Overbridge are all well advanced.

To facilitate construction works, and to ensure the safety of both the workforce and travelling public, substantial temporary traffic management measures are in place.



Randalstown West Overbridge under construction

These include:-

- a contraflow at the end of the M22, road closures, restricted speed limits, prohibited turning movements and reduced lane widths.
- a journey-time monitoring system installed to provide real time information about traffic journey time through the scheme, allowing action to be taken to minimise any delays.

Drone footage of progress is available on:-

<https://www.youtube.com/channel/UC7qq4Hmth9zxz3gTxA4D2RQ>

A29 Cookstown Bypass

The Regional Strategic Transport Network Transport Plan (RSTN TP) 2015 endorsed the A29 Cookstown Eastern Distributor now referred to as the A29 Cookstown Bypass.

Progress Report


The preferred route for the scheme, announced in 2010, involves the construction of approximately 4 kilometres of new single carriageway from the Dungannon Road Roundabout via the south of Cookstown, to a proposed new roundabout on the Moneymore Road at the north of the town. The scheme will also include sections of 2+1 and differential acceleration lanes to facilitate overtaking opportunities.

Owing to uncertainty relating to the availability of funding, it has not been possible to resume design development work on this project.

Progression of this scheme will be dependent upon the level of funding made available through future budgetary settlements and the relative priorities afforded to schemes competing for the available funds.



A5 Western Transport Corridor (A5WTC)

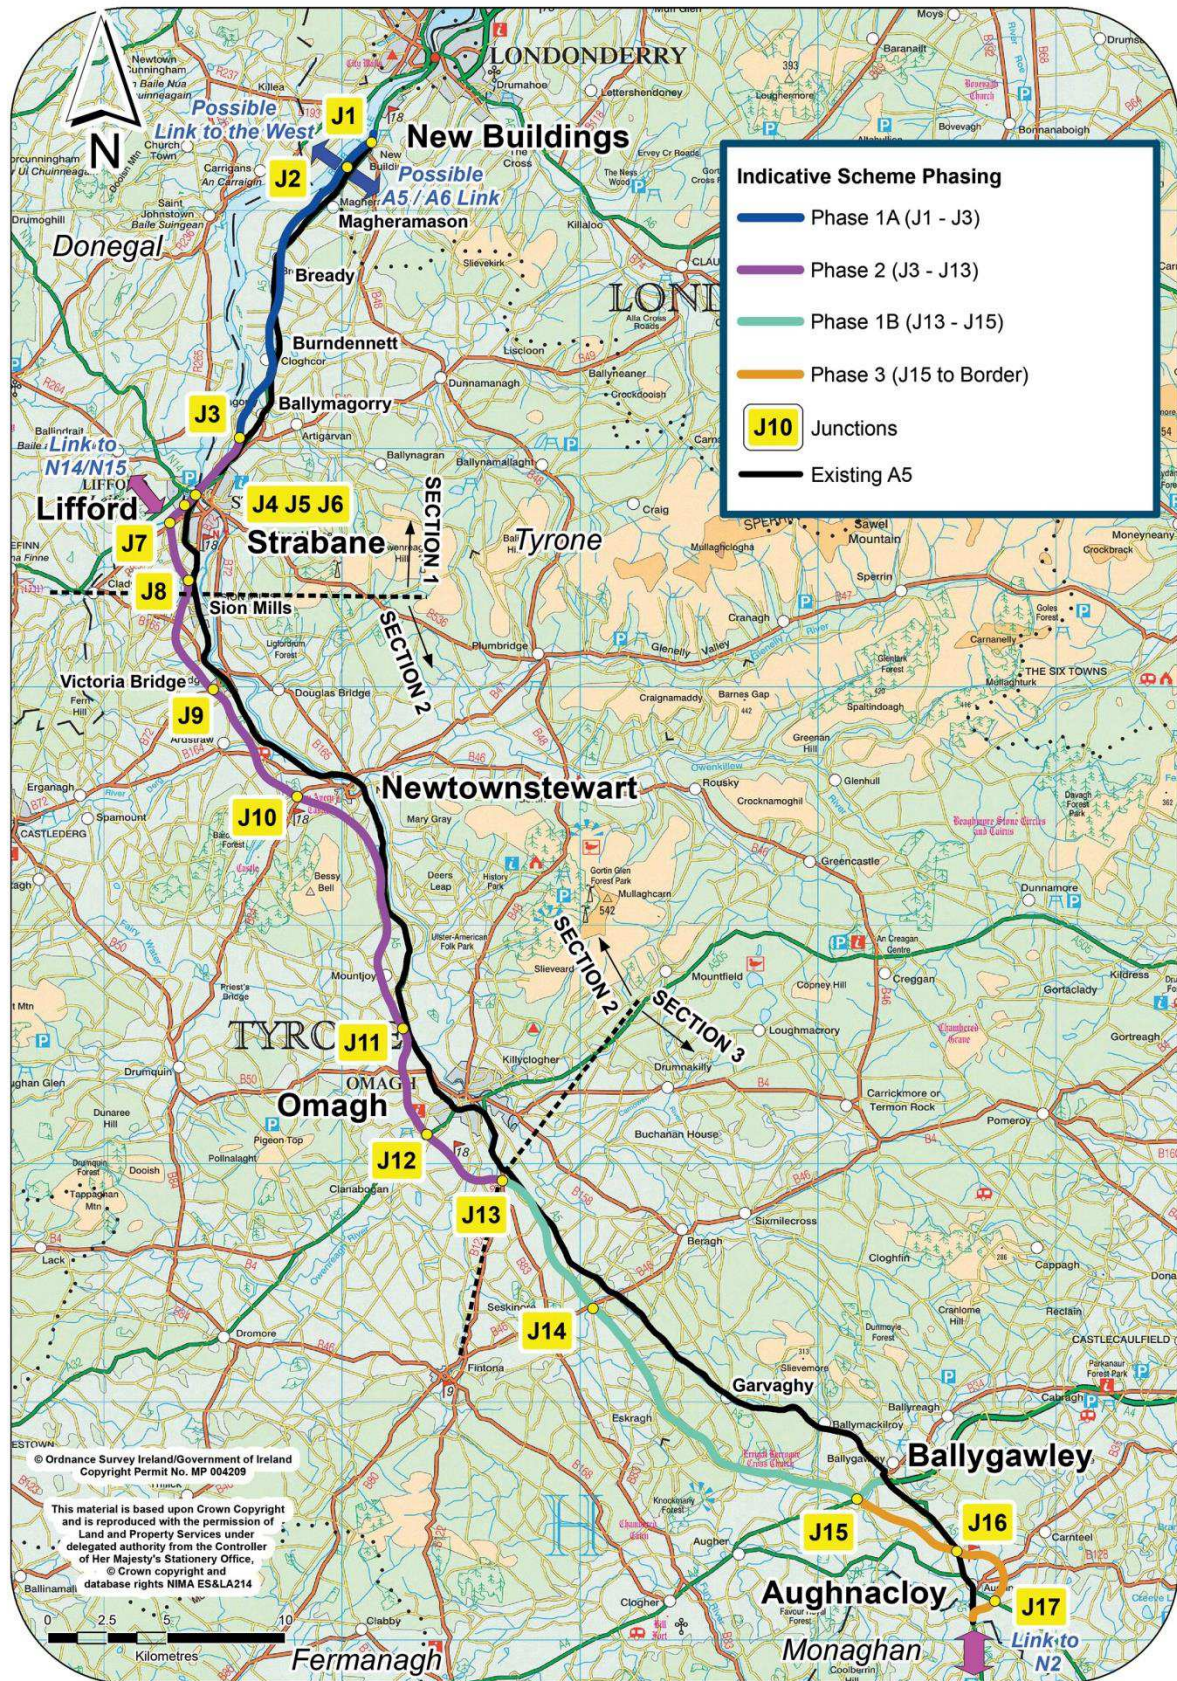

The A5 Western Transport Corridor (A5WTC) is a Northern Ireland Executive led scheme which aims to provide 85 kilometres (55 miles) of dual carriageway from south of Londonderry at New Buildings to the border at Aughnacloy.

In February 2016 the then Department for Regional Development (DRD) published for consultation the Notice of Intention to Make Vesting Orders (draft Vesting Orders) for a number of phases of the scheme as follows:

- Phase 1A - New Buildings to north of Strabane;
- Phase 1B - south of Omagh to Ballygawley; and
- Phase 2 - north of Strabane to south of Omagh.

The Notice of Intention to Make a Direction Order (i.e. draft Direction Order) for the length between New Buildings and Ballygawley and a new Environmental Statement (ES) covering the full extent of the scheme between New Buildings and Aughnacloy were also published during that time.

New draft Vesting Orders and a Direction Order for the section between Ballygawley and the border at Aughnacloy (Phase 3) are not being taken forward until details of the link with the N2 at the border with the Republic of Ireland have been clearly identified. This section was however included in the new Environmental Statement which must take account of the full extents of an overall project.

Following the public consultation into the draft orders and environmental statement for the scheme, the Department appointed the Planning Appeals Commission (PAC) as the independent inspector to administer a public inquiry. The inquiry was held in late 2016 and the PAC report was issued to the Department on 25 May 2017.

The Department is considering the recommendations from the PAC's report in detail before making a decision on whether to proceed with the scheme and make the necessary statutory Orders.

The Budget 2016/17 allocated an indicative amount of £229m between 2016/17 and 2020/21 to the A5 scheme. In line with 'A Fresh Start' Agreement; this includes a contribution from the Irish Government of £75m.

It is anticipated that the Decision to Proceed, together with the Departmental Statement and the Notice of Making of the Vesting Order for Phase 1A (New Buildings to North of Strabane) can be published in the coming weeks.

The Joint Venture Contractor for Phase 1A is BAM/Balfour Beatty & FP Mc Cann.

NETWORK MAINTENANCE

STRUCTURAL MAINTENANCE – 2017-18

Resurfacing

In the 2017-2018 financial year it is proposed to resurface the following roads at an estimated cost of £2.5 million in the Mid Ulster area.

Resurfacing Mid Ulster District (North)

Road No	Road Name	Length (m)	Status
A6	At the Elk Bar	320	Complete
A6	Glenshane Road at Lisnamuck	1765	Complete
A29	Moneysharvin Road, Swatragh	900	Complete
B160	Coagh Road, Stewartstown	900	Complete
B73	Drumconvis Road, Coagh	440	Complete
B73	Coagh Street Cookstown	150	Deferred due to gas main
B18	Loup Road, Moneymore	1200	Programmed
U0808	North Street, Pomeroy	240	Programmed
U5382	Springfield Park Bellaghy	400	On-Site

Subject to additional funding it is planned to resurface the following roads in the Mid Ulster District (North) area.

Road No	Road Name	Length (m)	Status
A29	Tobermore Road, Maghera	1300	Deferred
B160	North Street, Stewartstown	130	Deferred

Resurfacing Mid Ulster District (South)

Road No	Road Name	Length (m)	Status
A29	Cookstown Road	1100	Complete
A29	Stangmore Roundabout (Westside)	395	Complete
A29	Charlemont Street Moy	150	Complete
U7541	William Street Dungannon	194	Complete
B0035	Legilly Road Dungannon	400	Complete
B0043	Pomeroy Road Donaghmore	1200	Complete
B0106	Killyman St Moy	232	Complete
A0045	Oaks Road Dungannon	150	Programmed

Subject to additional funding it is planned to resurface the following roads In Mid Ulster (South) area

Road No	Road Name	Length (m)	Status
A4	Crossowen Road Augher	450	Pending
B106	Bush Road	590	Pending
B43	Newell Road	638	Pending
A45	Ballynakilly Road	750	Pending

Surface Dressing Mid Ulster District (North)

This year it is proposed to surface dress approximately 111kms of road in the Mid Ulster District.

Road No	Road Name	Length (m)	Status
B40	Moneyneany Road	1000	Deferred
C547	Lismoyle Road	2194	Complete
C547	Lismoyle Road	2143	Complete
C549	Drumbolg Road	2366	Complete
C550	Lurganagoose Road	500	Complete
C554	Sixtowns Road	2310	Complete
C557	Derganagh Road	503	Deferred
U5001	Portna Road	1486	Complete
U5019	Timaconway Road	1776	Complete
U5020	Killymuck Road	2930	Complete
U5022	Dunglady Road	2034	Complete
U5035	Carrowmenagh Lane	1000	Complete
U5050	Fallylea Road	1432	Complete
U5151	Blacks Road	1200	Deferred
U5154	Tullynagee Road	1695	Complete
U5155	Tullynagee Road	4937	Complete
U5157	Glenquilly Road	1335	Complete
U5160	Tirgan Road	903	Complete
U5160	Knockadoo Road	323	Complete
U5161	Tirgan Road	1696	Complete

U5161	Knockadoo Road	527	Complete
U5162	Letteran Road	464	Complete
U5167	Lecumpher Road	1680	Complete
U5170	Carmean Lane	1202	Complete
U5178	Mullaghboy Hill	1090	Complete
U5207	Cahore Road	1305	Complete
U5208	Cahore Road	1946	Complete
U5216	Davagh Road	2321	Complete
U5217	Davagh Road	283	Complete
U5239	Brackaghreilly Road	1996	Complete
U5243	Coolnasillagh Road	2625	Deferred
U5265	Dunlogan Road	2430	Complete
U5266	Ranaghan Road	1432	Complete
A505	Drum Road	2420	Deferred
B4	Pomeroy Road	3472	Complete
B73	Littlebridge Road	1035	Complete
B162	Lough Fea Road	1927	Complete
B181	Ruskey Road	2103	Complete
C612	Dunamore Road	622	Complete
C612	Tulnacross Road	3252	Complete
C612	Orritor Road	2604	Complete
C621	Teebane Road	1557	Complete
C622	Sandholes Road	1614	Complete
U602	Downs Road	1238	Complete
U715	Ballynagilly Road	3577	Complete
U716	Creevagh Road	1609	Complete
U716	Corby Road	1414	Complete
U717	Fegarron Lane	835	Complete
U718	Montober Road	2150	Complete
U720	Wellbrook Road	1687	Complete
U722	Drumearn Road	834	Complete
U723	Craigs Road	1450	Complete

U723	Drumnamalta Road	1655	Complete
U723	Craigs Road	1165	Complete
U725	Tullycall Road	2185	Complete
U820	Terrywinney Lane	2001	Complete
U825	Lammy Road	1090	Complete
U2203	Tullaghboy Road	2009	Complete
U2203	Ballyloughan Road	1479	Complete
U2206	Coltrim Road	1626	Complete
U2210	Tullynure Road	1857	Complete
U2216	Knockadoo Road	3079	Complete
U2217	Carrydarragh Road	1325	Complete
U2219	Drumeen Road	1616	Complete
U2219	Ivybank Road	1122	Complete
U2230	Spring Road	1695	Complete
U2242	Ballygonney Road East	1729	Complete
U715	Ballynagilly Road	3577	Complete

Surface Dressing Mid Ulster District (South)

Road No	Road Name	Length (m)	Status
A0029	Moy Rd (Hard Shoulders only)	2000	Complete
B0043	Pomeroy Rd	3000	Complete
B0045	Eglish Rd	2565	Complete
B0106	Bovean Rd	2150	Complete
B0161	Mountjoy Rd	840	Complete
C0635	Altnaglushan Rd	4426	Complete
C0636	Annaginny Rd	2881	Complete
C0640	Reenaderry Rd	1625	Complete
C0642	Annaghmore Rd	3411	Complete
C0648	Mullyneill Rd	850	Deferred
C0654	Springtown Rd	2368	Complete
C0654	Aghindarragh Rd	2153	Complete
C0654	Altadavan Rd	1383	Complete

C0655	Ashfield Rd	4465	Complete
C0656	Aghafad Rd	1555	Complete
U0318	Loughans Rd	3017	Deferred
U0326	Caledon Rd Spur	1526	Deferred
U0337	Youngs Rd	833	Deferred
U0421	Altadaven Rd	3689	Complete
U0423	Old Monaghan Road	555	Complete
U0426	Corick Rd	2146	Complete
U0426	Corrick Rd	1854	Complete
U0504	Bockets Rd	2858	Complete
U0516	Killens Rd	1318	Deferred
U0518	Carricklongfield Rd	1778	Deferred
U0518	Carricklongfield Rd	1757	Deferred
U0521	Gort Rd	2322	Deferred
U0521	Gort Rd	1205	Deferred
U0522	Cadian Road Spur	1564	Deferred
U0526	Creevelough Rd	1247	Deferred
U0541	Tannagh Lane	2195	Deferred
U0545	Ballyvaddy Rd	2834	Complete
U0901	Upper Cranlome Rd	3330	Deferred
U0901	Cranlome Rd	2847	Deferred
U0901	Altaglushin Rd	1395	Deferred
U0903	Lurgylea Rd	767	Deferred
U0907	Cappagh Rd	2008	Deferred
U0907	Cappagh Rd	2325	Complete
U0907	Toomog Rd	1502	Complete
U0909	Cornamaddy Rd	2051	Complete
U0916	Kilnaslee Rd	3040	Complete
U0916	Kerrib Lane	1433	Deferred
U0923	Mullaghrodden Rd	1715	Complete
U0923	Mullaghrodden Rd	559	Complete
U0923	Mullaghrodden Rd	795	Complete

U0923	Lisnagowan Rd	1250	Complete
U0924	Drumconnor Rd	1573	Deferred
U0925	Creevagh Rd	1482	Deferred
U0926	Derraghadoan Rd	1355	Complete
U0927	Lisnamonaghan Rd	293	Deferred
U0928	Aghareany Rd	2065	Deferred
U0937	Dredolt Rd	1322	Complete
U0938	Aghintober Rd	1535	Complete
U0938	Gortlenaghan Rd	1162	Deferred
U0939	Cabragh Rd	1962	Complete
U0939	Clonvaddy Rd	1920	Deferred
U0939	Clonavaddy Rd	2969	Deferred
U1017	Ferry Rd	3320	Complete
U1021	Derrytresk Rd	594	Complete
U1021	Derrytresk Rd	1138	Complete
U1025	Cloghog Rd	1884	Complete
U1025	Upper Meenagh Rd	868	Complete
U1028	Creenagh Lane	1432	Deferred
U1029	Coash Road	1740	Complete
U1033	Cohannon Rd	261	Complete
U1036	Mullaghmarget Rd	1500	Complete
U1104	Eskragh Rd	903	Deferred
U1105	Killybracken Rd	1616	Deferred
U1105	Killybracken Rd	657	Deferred
U1105	Killybracken Rd	242	Deferred
U1105	Killybracken Rd	513	Deferred
U1115	Drumflugh Rd	548	Complete
U1123	Syerla Rd	3633	Complete
U1125	Derryfubble Rd	1031	Complete
U1135	Bogbane Rd	1171	Complete
U1138	Dreemore Lane	1165	Deferred
U1410	Screeby Rd	1429	Deferred

U1411	Aghingowly Rd	2157	Complete
U1411	Aghingowly Rd	906	Deferred
U1411	Aghintain Rd Spur	816	Deferred
U7930	Hall Rd	97	Complete

Drainage Mid Ulster District (North)

This year it is proposed to carry out drainage improvements at the following locations:

Road No	Road Name	Proposal	Status
C553	Bancran Road	Upgrade existing drainage	Pending
C619	Curglasson	Investigate blocked pipe at Coagh Road	Pending
C621	Loughdoo Road	Replace pipe	Complete
C623	Tullyodonnell Road	Investigate blocked pipe	Complete
U220	Tullynure Road	Investigate water rising in verge	Complete
U625	Gortnaskea Road	Investigate water rising	Complete
U647	Annahavil Road	Upgrade existing drainage	Complete
U824	Gortfad Lane	Replace pipe filled with roots	Complete
U718	Montober Road	Update existing drainage system	Complete
U5125	Loves Road	Renew damaged culvert	Pending
U5174	Carmean Road	Renew soakaway	Pending
U5224	Bridge End	Investigate outfall from gully	Complete
U5319	Derrycrin Cottages	Investigate blocked gullies	Pending
U5335	Carsonville Drive	Install new gully	Pending

Drainage Mid Ulster District (South)

Road No	Road Name	Proposal	Status
B107	Clabby Rd	Replacement Pipe	Deferred
U0939	Clonavaddy Rd	New Drainage System	Deferred

Proposed footpath work Mid Ulster District (North)

Road No	Road Name	Status
C612	Orritor Road, Cookstown	Complete
U5005	Milburn Avenue, Cookstown	Complete
U5321	Brown Drive, Maghera	Deferred
U5341	Davison Villas, Castledawson	Complete
U5382	Glenelly Villas, Draperstown	Deferred

Proposed footpath work Mid Ulster District (South)

Local footway improvements will be carried out in conjunction with the resurfacing schemes.

Subject to additional funding it is planned to resurface the following footpaths:

Road No	Road Name	Status
F7007	Nelson Park, Fivemiletown	Pending
U7532	Empire Avenue, Milltown, Dungannon	Pending
F7532	Ashbeg Grove, Milltown, Dungannon	Pending
F7507	Fairmount Park, Dungannon	Pending

NETWORK DEVELOPMENT

LOCAL TRANSPORT AND SAFETY MEASURES

PLANNED WORKS 2017-2018

In the 2017-2018 financial year £340k has been allocated to the Division for Local Transport and Safety Measures within the Mid Ulster District Council area.

Carriageways

Road No	Road Name	Description	Status
A4	Ballagh Road/Ashfield Road Junction	Right turn lane to be provided in conjunction with resurfacing scheme	Design in Progress
U7506	Lisnahull Road/Newell Road, Dungannon	Widen Lisnahull carriageway at junction with Newell Road to provide dedicated right and left turn traffic lanes to ease congestion.	Substantially complete

Pedestrian Measures

Road No	Road Name	Description	Status
U7514	Quarry Lane, Dungannon	Provide pedestrian refuge island	Complete
C633	Whitebridge Road, Ballygawley	Provide a carriageway build out with tactile paving crossing points at junction with Main Street and adjacent to Saint Mary's Primary School.	Complete
A45	Ballygawley Road, Dungannon	Provide infill footway across bridge adjacent to Gormley's Motor Garage	Complete
B160	Ballyronan Road, Magherafelt	Provide Puffin crossing	Substantially Complete
B520	Hillhead Rd, Stewartstown	Provide approximately 60 metres of footway	In progress
B161	Mullanahoe Road, Ardboe	Provide approximately 60 metres of footway along Church frontage	In progress

C646	Killyliss Road, Eglish	Junction build out with tactile crossing	Complete
B73	Molesworth Street, Cookstown	Provide pedestrian refuge island	In progress
A29	Moneymore Road, Cookstown	Provide pedestrian refuge island	In progress
	Springhill Road, Moneymore	Provide pedestrian refuge island	In progress

Cycling Measures

Road No	Road Name	Description	Status
B34	Killyman Road	Provide footway/cycle track link between Gortmerron Link Road Junction and existing cycle track on Killyman Road adjacent to cemetery	Currently going through the vesting process to acquire the land.

Traffic Calming

Road No	Road Name	Description	Status
U5006	Forth Glen, Cookstown	Speed cushions to be provided and 20 mph limit	On hold
B45	Eglish Village	Speed cushions and gateway markings with advanced speed limit signage	Complete
U7506	Cloneen, Dungannon	Provide vertical traffic calming measures with gateway signage & a 20mph speed limit	Complete

Safer Routes to School (SRS)

Road No	School Name	Description	Status
C557	Knockloughrim Primary School	Provision of enhanced warning signs incorporating flashing warning lights, coloured surfacing, and road markings	Complete
B106	Killyman P.S. Killyman	Provision of enhanced warning signs incorporating flashing warning lights, coloured surfacing, and road markings	Complete
B34	Laghey P.S. Killyman	Provision of enhanced warning signs incorporating flashing warning lights, coloured surfacing, and road markings	Complete

Road Signs, markings and bollards

Road No	Road Name	Description	Status
A29	Tobermore	Upgrade directional signage	Complete
B73/ B161	Ardboe and Moortown area	Upgrade directional signage	In progress
U7543	Sloan Street, Dungannon	“No waiting at any time” restriction to replace an existing single yellow restriction	In progress
A4	Dual carriageway and roundabout, Ballygawley	Upgrade roundabout warning signs and chevron signs on roundabout to include high visibility backing boards. Also includes rumble strips on dual carriageway.	Complete
A4	Crossowen Road/ Ballagh Road	Upgrade directional signage along route between Ballygawley and council boundary at Fivemiletown	Pending
M1	Motorway	Provide directional signage to Tamnamore Park and Ride facility	Complete

B34	Killyman Road, Dungannon	Enhanced bend warning signage with edge of carriageway markings	Complete
-----	-----------------------------	---	----------

Speed limits

Road No	Road Name	Description	Status
C635	Lisnamonaghan Road, Castlecaulfield	Extend existing 30mph speed limit	Complete
B34	Tamnamore Road, Tamnamore	Reduce part of the existing 40mph limit to 30mh from Annaghbeg Road to Verners Bridge	Complete
C652	Old Dungannon Road, Ballygawley	Extend existing 30mph speed limit	Complete
B43	Pomeroy Road (Skea)	Provide a 50mph speed limit	Complete
U1029	Coash Road, Ballynakilly	Provide a 30mph speed limit	Complete
U7506	Cloneen, Dungannon	Provide a 20mph speed limit	Complete

Accessible Parking

Road No	Road Name	Description	STATUS
C633	Main St, Ballygawley	Disabled parking bay	Complete
C0612	Orritor Road, Cookstown	Disabled parking bay	In progress
U5009	Sullenboy Park Cookstown	Disabled parking bay	In progress
U5303	Queens Avenue Magherafelt	Disabled parking bay	In progress

It is intended that the following Local Transport and Safety Measures schemes will be progressed to detailed design and land acquisition stage. If additional funding becomes available during the financial year, it may permit some of these schemes to progress to the construction stage.

Road No	Road Name	Description	Status
A45	Ballynakilly Road at Greenagh Bridge, Coalisland	Bridge replacement & carriageway realignment	Detailed design progressing
A45	Granville Road, Dungannon	Road widening and realignment	Deferred
A29	Cookstown Road, Dungannon	Removal of bridge parapets to provide 2m grass verges	Deferred
A45	Granville Road at Killymaddy Knox, Dungannon	Provide missing footway link	Design progressing for potential delivery year 2018/19
B162	Disert Road, Draperstown	Forward sightline improvement	Detailed design progressing in association with Structures Unit and Section Office.
B160	Drumballyhugh / Gortvale, Pomeroy	Sightline improvement	Detailed design progressing
A29	Moy Road/Main Road, Moygashel Junction, Dungannon	Upgrade traffic signal installation to include "Toucan" cyclist facility and to install Microprocessor Optimised Vehicle Actuation (MOVA) system to improve efficiency of signalised junction	Detailed design has been completed

A4	Crossowen Rd, Clogher	Cycleway provision from Augher to Clogher	Deferred
A505	Drum Road at Dunamore Junction, Cookstown	Provision of undertaking lane	Detailed design progressing for potential delivery 2018/19
U5006	Forth Glen, Cookstown	Speed cushions to be provided	Detailed design progressing for potential delivery 2018/19
C560/ U5112	Aughrim Road/Gracefield Road junction, Magherafelt	Junction realignment with sightline improvements	A smaller white lining scheme has been completed and will continue to be monitored.
A29	Westland Road/Morgans Hill/Orritor Road Junction	Upgrade traffic signal installation to include “Toucan” cyclist facility and to install Microprocessor Optimised Vehicle Actuation (MOVA) system to improve efficiency of signalised junction	Detailed design has been completed

STRUCTURES

PLANNED WORKS 2017/18

During 2017-2018 Bridge Management Section intends to carry out work to structures in the Mid Ulster District Council area representing an investment of approximately £100k in the local infrastructure.

Bridge No/ Road No	Bridge Name, Location	Description of proposed work	Status
70739 / U5053	Milltown Bridge, Craigadick Road, Maghera	Extend existing structure with flexi-arch	Complete
61762 / C563	Ardtrea Bridge Littlebridge Road, Coagh	An options study has been completed. The design of a new replacement bridge is in progress. The 7.5 tonne interim weight restriction remains in place.	Programmed
61259 / A29	Drumraw Bridge Dungannon Road, Cookstown	It is proposed to replace the existing steel bridge parapets.	Programmed
61812 / U1019	Derrytresk Bridge, Derryvaren Road, Tamnamore, Dungannon	Bridge Replacement	Complete
70810 / U255	Boherdaile Bridge, Moneyneany	It is proposed to replace the existing bridge parapet fencing and repair inverts.	Programmed
70627 / B18	Newbridge New, Creagh Road, Magherafelt	It is proposed to repair and paint the existing bridge parapets.	Programmed
61809 / A29	Feenan Beg Bridge, Moneymore	It is proposed to repaint the existing bridge parapets	Programmed

On the 22 August 2017 there was a significant rainfall event across the NW of the province. Met Office reports confirmed 55.2 mm of rain fell within 24 hours, most of it falling in a 4 hour period. Approximately 63% of the average August rainfall fell in the affected area within an 8-9 hour period.

Some 650 bridges located in the Division were affected by the resulting flooding. An assessment of these bridges identified a total of 89 bridges needing urgent repairs or in some cases total replacement.

Within Mid Ulster Council Area, Nutgrove bridge No 70896, on C555 Iniscarn Road, Desertmartin, was destroyed and will have to be replaced.

STREET LIGHTING

PLANNED WORKS 2017/18

In the 2017-2018 financial year £210,000 has been allocated for capital street lighting works within the Mid Ulster District Council area. This will be used to continue our general programme of improvement/replacement of older systems.

Opportunity will also be taken to improve street lighting in areas where other street works are planned.

Street lighting faults can now be reported on the NIDirect website www.nidirect.gov.uk/services/report-street-light-fault or by phoning the new call centre on 0300 200 7899.

The following street lighting works are currently planned for 2017-2018.

SCHEME TITLE	SCHEME DESCRIPTION	STATUS
Car Park Transfers in Dungannon, Cookstown & Magherafelt Town Centres	Completion of Street Lighting Alteration Schemes commenced in 2015/16	Work Progressing
Ranfurly Crescent, Dungannon	Completion of street lighting renewal scheme commenced 2015/16	Completed
Aghereany Road, Donaghmore	Completion of street lighting renewal scheme commenced 2015/16	Completed
Pomeroy Road & Hillview Avenue Donaghmore	Completion of street lighting renewal scheme commenced 2015/16	Completed
Castle Drive, Caledon	Completion of street lighting renewal scheme commenced 2015/16	Completed
Kilgowney Close, Caledon	Completion of street lighting renewal scheme commenced 2015/16	Completed
Hillcrest Park, Aughnacloy	Completion of street lighting renewal scheme commenced 2015/16	Completed
Dungannon Road, Aughnacloy	Street Lighting Renewal Scheme	Completed

Station Road, Clogher	Extension of Street Lighting Area	Completed
Crawfordsburn, Maghera	Completion of street lighting renewal scheme commenced 2015/16	Completed
Princess Drive & Close, Magherafelt	Completion of street lighting renewal scheme commenced 2015/16	Completed
Mullaghboy Crescent, Magherafelt	Completion of street lighting renewal scheme commenced 2015/16	Completed
Sperrin View, Magherafelt	Completion of street lighting renewal scheme commenced 2015/16	Completed
Beechgrove Heights, Magherafelt	Completion of street lighting renewal scheme commenced 2015/16	Completed
Dunmore Close & Crescent, Cookstown	Completion of street lighting renewal scheme commenced 2015/16	Completed
Church View & Moneyhaw Road, Drumullan	Street Lighting Renewal Scheme	Completed
Claggan Park, Cookstown	Street Lighting Renewal Scheme	Completed
Windsor Crescent, Coagh	Completion of street lighting renewal scheme	Completed
